



Facilities & Planning

Hemet High Modernization & Expansion

Construction Progress Photo Report
May 2011

Building "D"

2/2/11: Electrical sweeps installed into the new electrical building.



Electrical Building "D"

Edison electrical vault and transformer pad are in place and awaiting flatwork to secure in place.



Electrical Building "D"


April 11, 2011: SOG is in the process of being poured.

April 12, 2011: Completed SOG.



Electrical Building "D"

April 28, 2011: Building has been framed and sheeted.
Fencing has been installed since the switch gear was secured into place prior to framing operations.

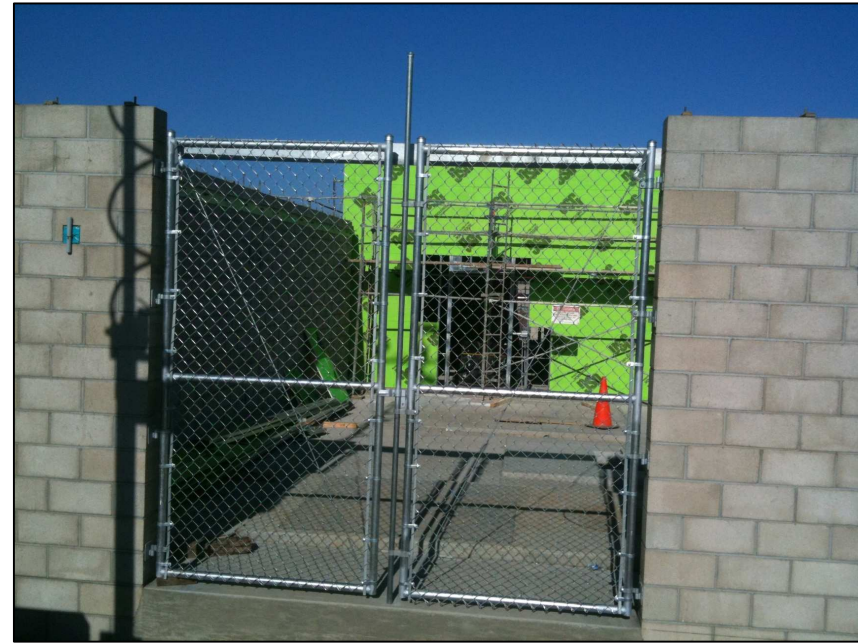

Electrical Building "D"

April 29, 2011: Building sheeting is finishing up and work on the parapet is just getting underway.



Retaining Wall

Retaining Wall-2/9/11: Nelson Studs have been installed and the waterproofing and rebar will commence at weeks end.



Retaining Wall

Retaining Wall-2/15/11: Drainage panel installed and rebar reinforcing in progress.



Retaining Wall

3/2/11: Retaining wall completed



Building C

1/26/11: Completed column embeds and grade beams in background. Elevator pit and the elect. data and bathroom footings in progress 2/2/2011



Building C

3/10/11: Slab Pour in progress



Building C

3/11/11: Slab on Grade Completed
Creteseal Application in progress



Classroom Building "C"

April 4, 2011: Steel erection began today.

April 5, 2011: The majority of the buildings
columns have been raised.



Classroom Building "C"

April 13, 2011: Structural steel is being set into place progressing towards the south end of the building. Second floor beam being set into place.



Classroom Building "C"

4/28/11: Structural Steel Erection continues. Safety cabling system is being installed for the decking installation.



Building C

5/5/11: 2nd floor deck has been spread and is in the process of being attached to the beams.



Science Building "B"

April 29, 2011: Footing construction continues.

5/5/11: Footings are reinforced and embed steel is being set into position.



School Entry Ramp

April 28, 2011: The footings for the switch back ramp situated between building "C" and "B" is getting underway.



Theater Building "A"

April 21, 2011: Electrical and Plumbing underground are underway.



Theater Building "A"

April 28, 2011: The sloped seating area, orchestra pit and front of stage have been excavated.



Building A

5/5/11: Footing construction has been completed at stage and orchestra pit. Reinforcing is currently underway including setting embed steel.



Aerial Photos

April 29, 2011: Building "C" in the foreground

April 29, 2011: Theater Building "A" in the foreground.

