Cash Flow Fund 21

as of 9/13/07

| Date | Month's Activity | Cash Balance | |
|----------|-------------------------|---|--|
| 07/01/07 | | 56,033,495.56 | - |
| 07/31/07 | (4,334,272.92) | 51,699,222.64 | |
| 08/30/07 | (4,698,467.81) | 47,000,754.83 | |
| 09/30/07 | (6,500,000.00) | 40,500,754.83 | |
| 10/26/07 | (7,500,000.00) | 33,000,754.83 | Pay off Sun Trust Lease using \$1M of Measure E Money |
| 11/30/07 | (6,500,000.00) | 26,500,754.83 | , and a second country |
| 12/31/07 | (6,500,000.00) | 20,000,754.83 | |
| 01/31/08 | (6,500,000.00) | 13,500,754.83 | |
| 02/28/08 | (6,500,000.00) | 7,000,754.83 | |
| 03/31/08 | (6,500,000.00) | 500,754.83 | sell bonds in March |
| | 30,000,000.00 | 30,500,754.83 | Esperance Anti-Action State of Control of Co |
| 04/30/08 | (6,500,000.00) | 24,000,754.83 | |
| 05/31/08 | (6,500,000.00) | 17,500,754.83 | |
| 06/30/08 | | 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1 - | |
| 06/30/08 | | | |
| | | | |

Figures in italics are estimates

Hemet Unified School District Measure T Bond Summary Report

| School Site Acacia | Current Budget | Interest | Committed | |
|----------------------------|---------------------|-----------------|------------------|----------------|
| | 150,000.00 | toroot | To Date | Balance |
| Bautista Creek | 50,000.00 | | 133,750.00 | 16,250.00 |
| Cottonwood | 2,500,000.00 | | 1,410.23 | 48,589.77 |
| Hamilton | 500,000.00 | | 2,467,862.07 | 32,137.93 |
| Hemet El | 200,000.00 | | 356,395.33 | 143,604.67 |
| Hemet High | 3,500,000.00 | 20.000.00 | 101,960.00 | 98,040.00 |
| ldyllwild | 80,000.00 | 32,898.00 | 3,532,533.81 | 364.19 |
| Little Lake | | 69,770.00 | 149,750.04 | 19.96 |
| Ramona | 200,000.00 | | 123,555.89 | 76,444.11 |
| Santa Fe | 500,000.00 | | 444,732.59 | 55,267.41 |
| Valle Vista | 200,000.00 | | 35,818.56 | 164,181.44 |
| West Valley High | 20,000.00 | | 6,740.45 | 13,259.55 |
| Whittier | 600,000.00 | | 560,945.45 | 39,054.55 |
| Winchester | 100,000.00 | | 81,602.28 | 18,397.72 |
| Tahquitz High School | 400,000.00 | | 113,148.87 | 286,851.13 |
| Rancho Viejo Middle | 25,000,000.00 | | 26,432,888.90 | (1,432,888.90) |
| Page Ranch | 24,000,000.00 | | 16,416,398.25 | 7,583,601.75 |
| | 1,000,000.00 | | 789,773.26 | |
| Currie Ranch | 1,000,000.00 | | 848,087.95 | 210,226.74 |
| Issuance Costs | 750,450.00 | | 338,205.05 | 151,912.05 |
| Interest (to be disbursed) | - | 912,054.00 | 330,203.05 | 412,244.95 |
| | | 5 12,004.00 | | 912,054.00 |
| Total | \$ 60,750,450.00 \$ | 1,014,722.00 \$ | 52,935,558.98 \$ | 8,829,613.02 |

Expenditure Report

Acacia Middle School

Plumbing, electrical, mechanical systems and plant/classroom repairs, campus security, safety, technology and accessibility projects, facility equity augmentation and equipment.

| Current Bond Budget | \$ 1. | 50,000.00 |
|---------------------|-------|-----------|
| Committed to Date | | 33,750.00 |
| Balance | | 16,250.00 |

Hemet Unified School District

| | Tana (70) measure | Bond - 1 detail record | \$133,750.00 | \$0.00 | \$133,750.00 |
|--|------------------------------|------------------------|--------------------|---------------------|--------------|
| | Totals for Fund (70) Measure | T Donat d L | | \$0.00 | \$133,750.00 |
| Fund (70) Measure T Bond douglas e barnhart | Construction Management | C12131 | \$133,750.00 | \$0.00 | 4.707 |
| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
| ACACIA MEASURE T BOND | Project# Measure T Ac | acia | | | |

Expenditure Report

Bautista Creek

Campus security, safety,technology and accessibility projects, facility equity augmentation and equipment, replace portable classrooms

| Current Bond Budget | \$ | 50,000.00 |
|---------------------|----|-----------|
| Committed to Date | · | 1,410.23 |
| Balance | \$ | 48,589.77 |

Hemet Unified School District

BAUTISTA CREEK MEASURE T BOND

| | Totals for Fund (70 |) Measure T Bond - 1 detail record | \$1,410.23 | \$1,410.23 | \$0.00 |
|---|--|------------------------------------|--------------------|---------------------|---------|
| | I TOTAL SECTION SECTIO | P59949 | \$1,410.23 | \$1,410.23 | \$0.00 |
| Fund (70) Measure T Bond Tri Best Visual Display Prod | White Boards | | L | | |
| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
| SACTION ONCER MEASURE I BONI | Project# Me | easure T Bautista | | | |

Expenditure Report

Cottonwood

Water well and fire protection, water conservation, Plumbing, electrical, mechanical systems and plant/classroom repairs, campus security, safety, technology and accessibility projects, facility equity augmentation and equipment.

Current Bond Budget *

\$ 2,500,000.00

Committed to Date

2,467,862.07

Balance

\$ 32,137.93

^{*} Additional \$500,000 to be allocated from 07/08 bond sale

Hemet Unified School District
COTTONWOOD MEASURE T BOND

Project# Measure T Cottonwood

| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
|---|--|-------------------|--------------------|----------------------|--------------------|
| Fund (70) Measure T Bond | | | | | Dalarice |
| All American Inspection Barnhart Labor Compliance | In Plant Inspection | P59132 | \$650.00 | \$650.00 | \$0.0 |
| Caldwell Land Surveys | Labor Compliance Services | C1220062 | \$19,545.00 | \$0.00 | \$19,545.0 |
| Caldwell Land Surveys | Topographic Survey for Well | P58766 | \$2,100.00 | \$2,100.00 | - 30 THE STREET |
| Creative Contractors | Survey | P6000028 | \$10,100.00 | \$6,060.00 | \$0.0 |
| Creative Contractors | Remove & Reinstall Swing | P59612 | \$2,800.00 | \$2,800.00 | \$4,040.0 |
| | Relocate Climber | P6001181 | \$2,400.00 | \$0.00 | \$0.00 |
| douglas e barnhart | Construction Management | C12121 | \$175,000.00 | \$113,803.00 | \$2,400.00 |
| douglas e barnhart Trust Acct | Trust Account | C12155 | \$1,806,277.00 | \$521,876.70 | \$61,197.00 |
| Geovision | Geophysical Survey | P58833 | \$3,700.00 | \$3,700.00 | \$1,284,400.30 |
| Hadley Tow | Move 5 Containers | P6000629 | \$975.00 | \$975.00 | \$0.00 |
| nland Foundation Eng Inc | Percolation Investigation | P59889 | \$10,350.00 | \$10,350.00 | \$0.00 |
| nland Foundation Eng Inc | Construction Testing | P6000132 | \$20,312.00 | \$8,673.50 | \$0.00 |
| nland Foundation Eng Inc | Trench Inspection | P6001183 | \$4,900.00 | \$0.00 | \$11,638.50 |
| Kevin Waite | Inspection | C12124 | \$10,000.00 | \$8,260.00 | \$4,900.00 |
| Modular Structures | 1 relocatable classroom and 1 restroom | P59137 | \$160,583.00 | \$136,424.70 | \$1,740.00 |
| JHM | Architect Fees | C11734 | \$125,625.00 | \$25,125.00 | \$24,158.30 |
| JHM | Architect Fees Well and Tank System | C11946 | \$103,893.13 | \$86,110.82 | \$100,500.00 |
| Riverside County Clerk | Filing Fee for CEQA | CL120961 | \$64.00 | \$64.00 | \$17,782.31 |
| afety Screens | Safety Screens | P59870 | \$1,055.10 | | \$0.00 |
| an Jacinto Electric | Electrical Work | P59654 | \$3,037.50 | \$1,055.10 | \$0.00 |
| ladden Engineering | Soil Engineering & Sewage Disposal Feasibility | P59127 | \$3,500.00 | \$3,037.50 | \$0.00 |
| hompson Engineering | Connect New Portables to Communication System | P6000027 | \$995.34 | \$3,500.00 \$0.00 | \$0.00 \$995.34 |
| 20.20 | Totals for Fund (70) Measure T Bond - | 22 detail records | \$2,467,862.07 | \$934,565.32 | \$1,533,296.75 |

District: Hemet Unified School District

Expenditure Report .

Hamilton

Permanent classroom additions, replacement of portable classrooms.

Plumbing, electrical, mechanical systems and plant/classroom repairs, campus security, safety, technology and accessibility projects, water conservation, facility equity augmentation and equipment.

| Current Bond Budget | \$ 50 | 0,000.00 |
|---------------------|-------|----------|
| Committed to Date | 35 | 6,395.33 |
| Balance | \$ 14 | 3 604 67 |

Hemet Unified School District HAMILTON MEASURE T BOND

Project# Measure T Hamilton

| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
|-------------------------------|----------------------------------|--------------------------|---------------------------|---------------------|-------------|
| Fund (70) Measure T Bond | | | | | |
| All American Inspection | In Plant Inspection | P59131 | | | |
| douglas e barnhart | Construction Management | | \$300.00 | \$300.00 | \$0.00 |
| douglas e barnhart | Construction Management | C12132 | \$43,750.00 | \$6,202.00 | \$37,548.00 |
| nland Foundation Eng Inc | | C12133 | \$13,750.00 | \$5,000.00 | \$8,750.00 |
| Glenna Construction | Construction Testing | P6000133 | \$8,112.00 | \$4,355.40 | \$3,756.60 |
| | Site Prep & Relo Installation | P6000130 | \$169,999.00 | \$161,678.30 | |
| Cevin Waite | Inspection | C12126 | \$5,000.00 | | \$8,320.70 |
| Modular Structures | 24 X 60 Modular Office Classroom | P59139 | 0.00 × 0.00 × 0.00 × 0.00 | \$2,660.00 | \$2,340.00 |
| lorth American Fence & Supply | Fencing | P6000158 | \$70,950.00 | \$62,299.80 | \$8,650.20 |
| JHM | Architect Fees | 03/3-25-2-2 | \$19,370.00 | \$0.00 | \$19,370.00 |
| afety Screens | Safety Screens | C1220007 | \$20,000.00 | \$17,847.32 | \$2,152.68 |
| hompson Engineering | | P59871 | \$3,237.04 | \$3,237.04 | \$0.00 |
| | Speaker Installation | P59874 | \$1,927.29 | \$0.00 | \$1,927.29 |
| | Totals for Fund (70) Measure T I | Bond - 11 detail records | \$356,395.33 | \$263,579.86 | \$92,815.47 |

Expenditure Report

Hemet Elementary

Plumbing, electrical, mechanical systems and plant/classroom repairs, campus security, safety, technology and accessibility projects, facility equity augmentation and equipment.

| Current Bond Budget | \$ 200,000.00 |
|---------------------|------------------|
| Committed to Date | 101,960.00 |
| Balance | \$ 98,040.00 |

Hemet Unified School District HEMET EL MEASURE T BOND

Project# Measure T Hemet EI

| | Totals for Fund (70) Measure 1 | Bond - 3 detail records | \$101,960.00 | \$497.00 | \$101,463.00 |
|---------------------------|--|--|-------------------------|---------------------|-------------------------|
| | Totals for Fund (70) Manager | | \$5,000.00 | \$0.00 | \$5,000.00 |
| Noviii Walte | Inspection | C12123 | \$5,000.00 | | |
| Kevin Waite | The second secon | P6000030 | \$96,250.00 \$710.00 | \$497.00 \$0.00 | \$95,753.00 \$710.00 |
| Inland Foundation Eng Inc | Construction Testing | FILES TO THE STATE OF THE STATE | | | |
| douglas e barnhart | Construction Management | C12134 | | | |
| Fund (70) Measure T Bond | | | | | |
| vendor | Description Contract | | Amount | Payments to Date | Balance |
| Vendor | Contract | PO#/ | Contract | - | |
| | Project# Measure T H | lemet El | | | |

Hemet Unified School District Expenditure Report

Hemet High

Plumbing, electrical, mechanical systems and plant/classroom repairs, campus security, safety, technology and accessibility projects, facility equity augmentation and equipment.

| Current Bond Budget * | \$ 3,500,000.00 |
|-----------------------|--------------------|
| Interest | 32,898.00 |
| Committed to Date | 3,532,533.81 |
| Balance | \$ 364.19 |

^{*} Additional \$22,500,000 to be allocated from 07/08 bond sale Additional \$5,000,000 to be allocated from 08/09 bond sale

Hemet Unified School District
HEMET HIGH MEASURE T BOND

Project# Measure T Hemet High

| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
|------------------------------------|--|-------------------|--------------------|---------------------|----------------|
| Fund (70) Measure T Bond | | | | | Dalance |
| Aardvark Clay & Supplies | Clay Pugmill Mixer | P58846 | | | |
| Barnhart Labor Compliance Services | Labor Compliance Services | C12101 | \$3,259.44 | \$3,259.44 | \$0.00 |
| Bills Fence | Fencing | P6001227 | \$65,720.00 | \$11,709.00 | \$54,011.00 |
| Creative Contractors | Remove Existing Foul Poles & Install New | P6000052 | \$2,665.00 | \$0.00 | \$2,665.00 |
| Dave Bang Assoc | Foul Poles | | \$7,800.00 | \$0.00 | \$7,800.00 |
| Department of General Services | CMAS Fees for Spectrum | P6000036 | \$9,096.26 | \$9,096.26 | \$0.00 |
| Division of State Architect | DSA Plan Check Fee | CL124095 | \$304.15 | \$304.15 | \$0.00 |
| douglas e barnhart | Construction Management | CL123352 | \$4,814.20 | \$4,814.20 | \$0.00 |
| douglas e barnhart | Construction Management | C12119 | \$100,000.00 | \$16,639.00 | \$83,361.00 |
| douglas e barnhart | Trust Acct Phase 3 | C12140 | \$423,392.00 | \$132,746.00 | \$290,646.00 |
| First American Title | Title Search | C12149 | \$1,148,000.00 | \$1,030,162.50 | \$117,837.50 |
| Flores Lund Consultants | Survey Mapping | CL123120 | \$750.00 | \$750.00 | \$0.00 |
| Flores Lund Consultants | | P59825 | \$18,212.00 | \$8,694.00 | \$9,518.00 |
| nland Foundation Eng Inc | Civil Engineering & Traffic Engineering | P6000684 | \$24,694.00 | \$9,255.72 | \$15,438.28 |
| aguna Clay Co | Compaction Testing Gas Kiln | P58945 | \$16,190.00 | \$15,647.87 | \$542.13 |
| Martin Container | | P59641 | \$11,933.84 | \$11,933.84 | \$0.00 |
| Pacific Alarm | Rent Storage Container for Temporary Storage | P59141 | \$770.41 | \$770.41 | \$0.00 |
| PJHM | Alarm System Installation | P58414 | \$2,375.00 | \$2,375.00 | \$0.00 |
| San Jacinto Electric | Architect Fees | C11652 | \$28,164.04 | \$23,963.50 | \$4,200.54 |
| Spectrum Communications | Electrical Work | P59655 | \$1,183.83 | \$1,183.83 | \$0.00 |
| | Cabling | P58567 | \$14,060.78 | \$12,633.77 | \$1,427.01 |
| pectrum Communications | Remove Fiber from Team Room | P59610 | \$1,500.00 | \$1,500.00 | \$0.00 |
| hompson Engineering | Install Communication Equipment | P58415 | \$4,148.86 | \$0.00 | \$4,148.86 |
| rittipo Architecture & Planning | Architect Fees for Remodel | C12161 | \$1,643,500.00 | \$115,950.00 | \$1,527,550.00 |
| | Totals for Fund (70) Measure T Bond - | 23 detail records | \$3,532,533.81 | \$1,413,388.49 | \$2,119,145.32 |

District: Hemet Unified School District

Expenditure Report

ldyllwild

Plumbing, electrical, mechanical systems and plant/classroom repairs, campus security, safety, technology and accessibility projects, facility equity augmentation and equipment.

| Current Bond Budget | \$ 80,000.00 |
|---------------------|--------------|
| Interest | 69,770.00 |
| Committed to Date | 149,750.04 |
| Balance | \$ 19.96 |

Hemet Unified School District

IDYLLWILD MEASURE T BOND

Project# Measure T Idyllwild

| | Totals for Fund (70) Measure | T Bond - 5 detail records | \$149,750.04 | \$10,831.04 | \$138,919.00 |
|--|------------------------------|---------------------------|--------------------|---------------------|--------------|
| | | P59949 | \$6,597.04 | \$6,597.04 | \$0.00 |
| ri Best Visual Display Prod | Whiteboards | * | \$25,000.00 | \$0.00 | \$25,000.00 |
| JHM | Architect Fees | C1220055 | \$3,700.00 | \$3,700.00 | \$0.00 |
| Peter Gulassa | Retaining Wall | P58896 | \$51,328.00 | \$0.00 | \$51,328.00 |
| North American Fence & Supply | Fencing | P6000158 | \$63,125.00 | \$534.00 | \$62,591.00 |
| Fund (70) Measure T Bond douglas e barnhart | Construction Management | C12135 | 000 405 00 | NAC 255 | |
| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |

Expenditure Report

Little Lake

Plumbing, electrical, mechanical systems and plant/classroom repairs, campus security, safety, technology and accessibility projects, classroom replacements and building additions, facility equity augmentation and equipment.

| Balance | \$ 76.444.11 |
|---------------------|------------------|
| Committed to Date | 123,555.89 |
| Committed to Date | \$ 200,000.00 |
| Current Bond Budget | |

Hemet Unified School District

LITTLE LAKE MEASURE T BOND

Project# Measure T Little Lake

| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
|--|------------------------------|-------------------------|--------------------|--|---------------|
| Fund (70) Measure T Bond | | | | | Dalatioe |
| Bills Fence | Fencing | P6000092 | 00.005 | in the state of th | |
| Creative Contractors | Install Shade Shelter | | \$9,925.00 | \$9,925.00 | \$0.00 |
| Dave Bang Assoc | | P6000050 | \$9,900.00 | \$0.00 | \$9,900.00 |
| | Shade Shelter | P6000038 | \$14,754.77 | \$0.00 | \$14,754.77 |
| douglas e barnhart | Construction Management | C12136 | \$40,000.00 | | 5 1 6 V 6 D 6 |
| PCH Architects | Architect Fees Shade Shelter | P6000682 | | \$3,102.00 | \$36,898.00 |
| Peter Gulassa | Concrete Work | | \$9,000.00 | \$0.00 | \$9,000.00 |
| Thompson Engineering | III OLEMAN DE BANCO EL PRE | P6000070 | \$2,875.00 | \$2,875.00 | \$0.00 |
| The same of the sa | Communication System | P59657 | \$35,102.00 | \$28,432.62 | \$6,669.38 |
| Tot Turf by Robertson Industries | Repair Post Holes | P6000054 | \$1,999.12 | \$0.00 | \$1,999.12 |
| | Totals for Fund (70) Measure | T Pand Oder | | 40.00 | Ψ1,999.12 |
| | Tame for Fund (70) Measure | Bond - 8 detail records | \$123,555.89 | \$44,334.62 | \$79,221.27 |

Expenditure Report

Ramona

Plumbing, electrical, mechanical systems and plant/classroom repairs, campus security, safety, technology and accessibility projects, classroom replacements and building additions, facility equity augmentation and equipment.

| Current Bond Budget | \$ 500,000.00 |
|---------------------|------------------|
| Committed to Date | 444,732.59 |
| Balance | \$ 55,267.41 |

Hemet Unified School District RAMONA MEASURE T BOND

Project# Measure T Ramona

| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
|--|---|--------------------|-----------------------------|-----------------------|---------------------------|
| Fund (70) Measure T Bond | | | | | |
| All American Inspection Division of State Architect douglas e barnhart | In Plant Inspection DSA Plan Check Fees | P59134 CL119875 | \$600.00 \$900.00 | \$600.00 \$900.00 | \$0.00 \$0.00 |
| Inland Foundation Eng Inc | Construction Management | C12137 | \$210,000.00 | \$0.00 | \$210,000.00 |
| J Glenna Construction | Construction Testing | P6000031 | \$1,612.00 | \$0.00 | \$1,612.00 |
| Cevin Waite | Sidewalk | P6000034 | \$6,600.00 | \$6,600.00 | \$0.00 |
| Modular Structures | Inspection 24 x 40 Standard Modular Classroom | C12125 P59140 | \$5,000.00 | \$560.00 | \$4,440.00 |
| PCH Architects | Architect Fees | C12105 | \$124,268.00 \$20,000.00 | \$95,641.20 \$0.00 | \$28,626.80 |
| CH Architects | Architect Fees - 2 Relos | C12147 | \$9,700.00 | \$7,760.00 | \$20,000.00 \$1,940.00 |
| Lensen Co afety Screens | Site work & Install 2 Relocatable Classrooms | P6000039 | \$53,000.00 | \$47,700.00 | \$5,300.00 |
| an Jacinto Electric | Safety Screens | P59877 | \$1,960.20 | \$1,960.20 | \$0.00 |
| pectrum Communications | Electrical Work | P6001182 | \$1,200.00 | \$0.00 | \$1,200.00 |
| hompson Engineering | Install Cabling to Connect new Relos | P6000042 | \$8,050.38 | \$0.00 | \$8,050.38 |
| nompour Engineering | Connect Communication Systems to new Relos | P59875 | \$1,842.01 | \$0.00 | \$1,842.01 |
| | Totals for Fund (70) Measure T Bond - | 14 detail records | \$444,732.59 | \$161,721.40 | \$283,011.19 |

Expenditure Report

Santa Fe Middle School

Plumbing, electrical, mechanical systems and plant/classroom repairs, campus security, safety, technology and accessibility projects, facility equity augmentation and equipment.

| Current Bond Budget | \$ 200,000.00 |
|---------------------|------------------|
| Committed to Date | 35,818.56 |
| Balance | \$ 164,181.44 |

Hemet Unified School District

SANTA FE MEASURE T BOND

Project# Measure T Santa Fe

| ctrial Work Wood Shop lite Boards Totals for Fund (70) Measure | P6000628 P59949 | \$13,150.00 \$3,300.00 \$5,252.58 | \$13,150.00 \$0.00 \$5,252.58 | \$0.00 \$3,300.00 \$0.00 |
|--|--|---|--|---|
| ctrial Work Wood Shop | P6000628 | 11 - 1 0-01 | | The same |
| | Committee of the commit | 11 - 1 0-01 | | The same |
| | F0000620 | \$13.150.00 | | |
| model Fitness Room | Pennego | | | 1 55 1 797 |
| or Mats | P6000163 | \$2.815.48 | | \$0.0 |
| ncing | P58909 | \$11,300.50 | \$11 300 50 | \$0.0 |
| | | | | |
| Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
| | Description noing | Description P58909 P6000163 | Description P58909 \$11,300.50 For Mats P6000163 \$2,815.48 | Description Contract Contract Amount Payments to Date |

Hemet Unified School District Expenditure Report

Valle Vista

Campus security, safety, technology and accessibility projects, facility equity augmentation and equipment.

| Current Bond Budget | \$ 20 | ,000.00 |
|---------------------|--------|---------|
| Committed to Date | 6 | 740.45 |
| Balance | \$ 13, | 259.55 |

Hemet Unified School District

VALLE VISTA MEASURE T BOND

| | Totals for | Fund (70) Measur | e T Bond - 1 detail record | \$6,740.45 | \$6,740.45 | \$0.00 |
|---|-------------|---|----------------------------|--------------------|---------------------|---------|
| Fund (70) Measure T Bond Tri Best Visual Display Prod | Whiteboards | 11.1 ********************************** | P59949 | \$6,740.45 | \$6,740.45 | \$0.00 |
| Vendor | 4.1 | Contract escription | PO#/ Contract | Contract Amount | Payments to Date | Balance |
| VALLE VISTA MEASURE I BOND | Proje | ect# Measure T \ | Valle Vista | | | |

Expenditure Report

West Valley

Campus security, safety,technology and accessibility projects and site improvements, facility equity augmentation and equipment.

| Current Bond Budget | \$ 600,000.00 |
|---------------------|------------------|
| Committed to Date | 560,945.45 |
| Balance | \$ 39,054.55 |

Hemet Unified School District

WEST VALLEY MEASURE T BOND

Project# Measure T West Valley

| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
|--|--|-----------------------|--------------------|---------------------|--------------|
| Fund (70) Measure T Bond | | | | | |
| Bills Fence | Fencing | P6000621 | \$12,250.00 | £42.250.00 | |
| Creative Contractors | Remove existing and install new foul poles | P6000053 | | \$12,250.00 | \$0.00 |
| Dave Bang Assoc | Foul Poles, Benches, Bleachers | P6000035 | \$7,800.00 | \$7,800.00 | \$0.00 |
| douglas e barnhart | Construction Management | C12130 | \$16,220.95 | \$16,220.95 | \$0.00 |
| Flores Lund Consultants | Survey Mapping Services | | \$74,687.00 | \$7,509.00 | \$67,178.00 |
| Louies Nursery | Groundcover | C1220100 | \$15,550.00 | \$0.00 | \$15,550.00 |
| Peter Gulassa | Move & Reinstall Bleachers JV Field | P58938 | \$6,885.23 | \$6,885.23 | \$0.00 |
| Peter Gulassa | Install bleachers in Softball field | P6000047 | \$1,275.00 | \$1,275.00 | \$0.00 |
| РЈНМ | Architect Fees Gym Floor | P6000048 | \$4,850.00 | \$4,850.00 | \$0.00 |
| РЈНМ | | C1220005 | \$35,000.00 | \$33,250.00 | \$1,750.00 |
| San Jacinto Electric | Architect Fee Improvements | C1220054 | \$141,000.00 | \$14,100.00 | \$126,900.00 |
| Temecula Valley Pipe & Supply | Electrical Work | P6000627 | \$4,800.00 | \$0.00 | \$4,800.00 |
| District Control of the Control of t | Jute for Groundcover project | P58897 | \$1,777.27 | \$1,777.27 | \$0.00 |
| Vestern Flooring Inc | Replace Gym Floor | P6000157 | \$238,850.00 | \$174,285.00 | \$64,565.00 |
| | Totals for Fund (70) Measure T Bond | d - 13 detail records | \$560,945.45 | \$280,202.45 | \$280,743.00 |

Expenditure Report

Whittier

Plumbing, electrical, mechanical systems and plant/classroom repairs, campus security, safety, technology and accessibility projects, classroom replacements and building additions, facility equity augmentation and equipment.

| Current Bond Budget | \$ 100,000.00 |
|---------------------|---------------|
| Committed to Date | 81,602.28 |
| Balance | \$ 18.397.72 |

Hemet Unified School District

WHITTIER MEASURE T BOND

Project# Measure T Whittier

| | Totals for Fund (70) Measur | re T Bond - 2 detail records | \$81,602.28 | \$32,852.28 | \$48,750.00 |
|-----------------------------|-----------------------------|------------------------------|--------------------|---------------------|-------------|
| Man also V | | P59949 | \$32,852.28 | \$32,852.28 | \$0.00 |
| ri Best Visual Display Prod | White Boards | | \$48,750.00 | \$0.00 | \$48,750.0 |
| ouglas e barnhart | Construction Management | C12138 | | | |
| und (70) Measure T Bond | | | | | |
| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |

Expenditure Report

Winchester

Plumbing, electrical, mechanical systems and plant/classroom repairs, campus security, safety, technology and accessibility projects, classroom replacements and building additions, facility equity augmentation and equipment.

| Current Bond Budget | \$ 400,000.00 |
|---------------------|------------------|
| Committed to Date | 113,148.87 |
| Balance | \$ 286.851 13 |

Hemet Unified School District

WINCHESTER MEASURE T BOND

Project# Measure T Winchester

| Description Description Contract Payments to Date Balance | | Totals for Fund (70) Measure T Bo | nd - 6 detail records | \$113,148.87 | \$3,200.00 | \$109,948.8 |
|--|------------------------------|--|-----------------------|--|------------|-------------|
| Description Description Description Description Description Description Description Description Description Contract Amount Description Description Contract Amount Description Descript | | 1 Deliveration of Arts States | | \$15,007.26 | \$0.00 | \$15,007.2 |
| Description Description Description Description Description Description Description Description Description Contract Amount Payments to Date Balance Balance Fund (70) Measure T Bond Creative Contractors Remove old & Install new Shade Structure P6000051 P6000037 P6000037 P19,541.61 PCH Architects Achitect Fees for Shade Shelter P6000683 Peter Gulassa Description Contract Payments to Date Balance Contract Amount Payments to Date Balance Contract Amount Contract Payments to Date Balance Contract Amount P6000051 S16,400.00 S19,541.61 S0.00 S19,541.61 PCH Architects Achitect Fees for Shade Shelter P6000683 Peter Gulassa Install Whiteboards | Shiffler Equipment Sales Inc | Whiteboards | | | \$3,200.00 | \$0.0 |
| Pend (70) Measure T Bond Creative Contractors Remove old & Install new Shade Structure Pend St | Peter Gulassa | Install Whiteboards | | | | \$9,000.0 |
| Tend (70) Measure T Bond Creative Contractors Remove old & Install new Shade Structure Payments to Date Balance Contract Amount Contract Fund (70) Measure T Bond Creative Contractors Remove old & Install new Shade Structure P6000051 \$16,400.00 \$10,000 \$19,541.61 \$0.00 \$19,541.61 \$0.00 \$19,541.61 | PCH Architects | Achitect Fees for Shade Shelter | P6000683 | View Control Control | | |
| Vendor Description Contract Contract Amount Payments to Date Balance Fund (70) Measure T Bond Creative Contractors Remove old & Install new Shade Structure P6000051 \$16,400.00 \$0.00 \$16,400 Dave Bang Assoc Shade Structure P6000037 \$19,541,61 \$0.00 \$10,541 | | Construction Management | C12118 | \$50,000.00 | 15-114.5 | |
| Vendor Description Contract Contract Amount Payments to Date Balance Fund (70) Measure T Bond Creative Contractors Remove old & Install new Shade Structure P6000051 \$16,400.00 \$0.00 \$16,400.00 | | The state of the s | P6000037 | \$19,541.61 | \$0.00 | |
| Description Description Description Description Contract Amount Payments to Date Balance Fund (70) Measure T Bond Creative Contractors | Dave Bang Assoc | | P6000051 | \$16,400.00 | \$0.00 | \$16,400.0 |
| Vendor Description Contract Payments Contract Amount to Date Balance | Creative Contractors | Remove old & Install now Shade Co. | | | | |
| Vendor Description Contract Payments | Fund (70) Measure T Bond | | | | | Dulance |
| | Vendor | Contract Description | 555 | The state of the s | | Ralance |

Hemet Unified School District Expenditure Report Tahquitz High School

| Measure E Bond Allocation | 92 250 Miles (C.) |
|---|---------------------|
| Measure T Bond Allocation | \$ 15,618,397.00 |
| CFD's | 30,000,000.00 |
| 그것 때 그 그 그 그 그 그 그 그 그 그 그 그 그 그 그 그 그 그 | 9,038,141.00 |
| Savings from Harmony, McSweeny, Diamond Valley Developer Fees | 2,214,288.00 |
| | 4,231,512.00 |
| State Grant Budget | 30,369,098.00 |
| Design Money released from State | 7,496,640.00 |
| Energy Funding - OPSC | 1,184,459.00 |
| Interest | 228,536.27 |
| Total Budget | |
| Total Budget | 100,381,071.27 |
| | |
| Current Measure T Budget * | \$ 25,000,000.00 |
| 0 | T = 0,000,000.00 |
| Committed to Date | 26,432,888.90 |
| Manager T Dalaman | |
| Measure T Balance | \$ (1,432,888.90) |
| | |

^{*} Additional \$5,000,000 to be allocated from 07/08 bond sale.

Hemet Unified School District TAHQUITZ HIGH SCHOOL

Project# 50/67082-00-08

| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
|------------------------------------|---|------------------|------------------------------|---------------------|-----------------|
| Fund (70) Measure T Bond | | | | | |
| Ballard Gas Service | Propane System | P6000691 | \$533.67 | \$533.67 | \$0.00 |
| Barnhart Labor Compliance Services | Labor Compliance Services | C11769(70) | \$219,106.00 | \$33,511.00 | |
| Bogle Inspection Services | Inspection | C11814(70) | \$54,000.00 | \$40,800.00 | \$185,595.00 |
| Caldwell Land Surveys | Survey Phase 2 | P6000000 | \$19,000.00 | \$15,200.00 | \$13,200.00 |
| Caldwell Land Surveys | Survey for Phase III | P6001266 | \$33,500.00 | \$0.00 | \$3,800.00 |
| City of Hemet | Waste Removal | P53930(70) | \$28,335.97 | | \$33,500.00 |
| Dave Bang Assoc | Steel Bleachers | P58950 | \$9,552.41 | \$7,680.94 | \$20,655.03 |
| Division of State Architect | DSA Plan Check Fees | CL118575 | \$25,050.00 | \$0.00 | \$9,552.41 |
| douglas e barnhart | Construction Management Phase 2 | C12120 | \$1,000,000.00 | \$25,050.00 | \$0.00 |
| douglas e barnhart | Construction Management Phase 3 (Stadium) | C1220008 | \$962,471.00 | \$511,627.00 | \$488,373.00 |
| douglas e barnhart Trust Acct | Trust Acct for Phase 2 | C12154 | \$16,692,562.00 | \$24,696.00 | \$937,775.00 |
| douglas e barnhart Trust Acct | Trust Acct Phase 3 (Stadium) | C1220112 | Here's a market and a second | \$5,451,956.10 | \$11,240,605.90 |
| astern Municipal Water District | Plan Check Deposit | CL124366 | \$9,038,698.00 | \$0.00 | \$9,038,698.00 |
| astern Municipal Water District | Water Usage & Backflow Tests | CL124611 | \$4,000.00 | \$4,000.00 | \$0.00 |
| astern Municipal Water District | Water Usage | P6001179 | \$322.00 | \$322.00 | \$0.00 |
| mpire & Associates | Vault & Catch Basin Covers | P59879 | \$20,000.00 | \$0.00 | \$20,000.00 |
| lores Lund Consultants | Civil Engineering | C1220004 | \$875.00 | \$0.00 | \$875.00 |
| nland Foundation Eng Inc | Construction Testing Phase II | | \$5,000.00 | \$2,443.78 | \$2,556.22 |
| nland Foundation Eng Inc | Construction Testing Phase III | C12127 | \$221,307.00 | \$54,738.72 | \$166,568.28 |
| fark-Costello Co | Trash Compactors | C12128 | \$88,050.00 | \$14,616.25 | \$73,433.75 |
| lobile Storage Group | Relocate storage unit | P6000073 | \$21,857.00 | \$21,857.00 | \$0.00 |
| alsbury Industries | Courier Box | P6000744 | \$363.66 | \$0.00 | \$363.66 |
| an Jacinto Electric | Electrical Work | P59872 | \$628.36 | \$0.00 | \$628.36 |
| an Jacinto Electric | Electrical for Sump Pump | P6000626 | \$2,600.00 | \$0.00 | \$2,600.00 |
| pectrum Communications | Cabling Phase 2 | P6001180 | \$3,200.00 | \$0.00 | \$3,200.00 |
| | Cability Fliase 2 | P6000622 | \$359,243.32 | \$0.00 | \$359,243.32 |

District: Hemet Unified School District

Page 10 of 13

Hemet Unified School District

TAHQUITZ HIGH SCHOOL

Project# 50/67082-00-08

| 11468(70) 1220114 detail records | \$553,803.50 \$1,131,287.00 | \$0.00 \$553,803.50 \$0.00 | \$61,351.42 \$0.00 \$1,131,287.00 |
|--|--------------------------------|----------------------------------|---|
| | \$553,803.50 | | 2 8 - 2 0 4 0 5 1 1 2 7 1 4 - |
| 11468(70) | | | 2 8 - 2 0 4 0 5 1 1 2 7 1 4 - |
| | 401,001.42 | 20.00 | \$61 351 42 |
| 6000046 | \$61,351,42 | 60.00 | |
| | | | Dalance |
| Contract PO#/ Description Contract | | Payments to Date | Balance |
| | | Contract Amount | Contract Amount to Date |

To be paid by CFD's -4,123,808.41

Hemet Unified School District Expenditure Report Rancho Viejo Middle School

| Measure T Bond Allocation State Funds | \$ | 24,000,000.00 12,000,000.00 |
|---------------------------------------|----|--------------------------------|
| Total Project Budget | | 36,000,000.00 |
| | | |
| Total Bond Budget | \$ | 24,000,000.00 |
| Committed to Date | | 16,416,398.25 |
| Bond Balance | \$ | 7.583 601 75 |

Hemet Unified School District
RANCHO VIEJO MIDDLE SCHOOL

Project# New Middle #4

| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
|------------------------------------|--|------------------|--------------------|---------------------|----------------|
| Fund (70) Measure T Bond | | | | | |
| Armed Response Security | Construction Site Security | P6000685 | \$108,000.00 | \$6,000.00 | 0400 000 00 |
| Barnhart Labor Compliance Services | Labor Compliance | C11770 | \$241,900.00 | | \$102,000.00 |
| Building Systems Management | SCE Utility Rebate | P54442 | \$7,780.00 | \$33,888.00 | \$208,012.00 |
| Caldwell Land Surveys | Topographical Survey | P54884 | \$1,800.00 | \$7,002.00 | \$778.00 |
| Caldwell Land Surveys | Land Survey | P58829 | \$54,000.00 | \$1,800.00 | \$0.00 |
| California Dept of Education | Site Review Fee | CL110111 | \$12,419.85 | \$27,000.00 | \$27,000.00 |
| City of Hemet | Waste Removal | P58895 | | \$12,419.85 | \$0.00 |
| DEWCO | Food Facilities Design | P53184 | \$1,000.00 | \$988.98 | \$11.02 |
| Division of State Architect | DSA Fees | CL101330 | \$12,500.00 | \$8,125.00 | \$4,375.00 |
| Division of State Architect | DSA Fees | CL106934 | \$153,410.00 | \$153,410.00 | \$0.00 |
| Division of State Architect | DSA Plan Check Fee | CL120572 | \$8,055.00 | \$8,055.00 | \$0.00 |
| douglas e barnhart | Construction Management | C11744 | \$3,960.00 | \$3,960.00 | \$0.00 |
| douglas e barnhart Trust Acct | Trust Account | C12148(70) | \$1,250,000.00 | \$780,917.00 | \$469,083.00 |
| Eastern Municipal Water District | Plan Check Deposit | CL124051 | \$12,189,069.86 | \$3,346,358.80 | \$8,842,711.06 |
| astern Municipal Water District | Water Usage | CL125142 | \$4,000.00 | \$4,000.00 | \$0.00 |
| astern Municipal Water District | Water Usage | P6001265 | \$69.75 | \$69.75 | \$0.00 |
| stes Inspection Services | Inspection | C12102 | \$10,000.00 | \$0.00 | \$10,000.00 |
| nland Foundation Eng Inc | Construction Testing | | \$100,000.00 | \$31,500.00 | \$68,500.00 |
| nland Foundation Eng Inc | Preliminary Geotechnical Investigation | C12129 | \$351,960.00 | \$25,719.00 | \$326,241.00 |
| nland Foundation Eng Inc | Compaction & Material Testing | CL102725 | \$3,000.00 | \$3,000.00 | \$0.00 |
| acific Alarm | Outdoor Perimeter Alarm System | P54799 | \$19,470.00 | \$19,470.00 | \$0.00 |
| outhern California Edison | Establish Electrical Service | P58570 | \$11,038.00 | \$0.00 | \$11,038.00 |
| outhern California Edison | Electric Usage | CL119369 | \$16,451.10 | \$16,451.10 | \$0.00 |
| outhern California Edison | Electrical Usage | CL123177 | \$144.38 | \$144.38 | \$0.00 |
| hompson Engineering | Telecenter V System | P6000138 | \$40,000.00 | \$1,205.80 | \$38,794.20 |
| | relecenter v System | P59824 | \$117,060.10 | \$0.00 | \$117,060.10 |

District: Hemet Unified School District

Page 2 of 4

Hemet Unified School District

RANCHO VIEJO MIDDLE SCHOOL

Project# New Middle #4

| | Totals for Fund (70) Measure | T Bond - 27 detail records | \$16,416,398.25 | \$5,895,873.54 | \$10,520,524.71 | |
|----------------------------------|------------------------------|----------------------------|--------------------|---------------------|-----------------|--|
| Trittipo Architecture & Planning | Architect Fees | | | \$1,404,388.88 | \$283,111.12 | |
| Thompson Engineering | Bulletin Board System | P59828 | \$11,810.21 \$0.00 | | \$11,810.21 | |
| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance | |

Hemet Unified School District Expenditure Report Page Ranch

| Measure T Bond Allocation State Funds Total Project Budget | \$ 12,000,000.00 to be determined 12,000,000.00 |
|---|--|
| Current Measure T Budget * | \$ 1,000,000.00 |
| Committed to Date | 789,773.26 |
| Bond Balance | \$ 210,226.74 |

^{*} Additional \$1,000,000 to be allocated from 07/08 bond sale. Additional \$10,000,000 to be allocated from 10/11 bond sale

Hemet Unified School District PAGE RANCH ELEMENTARY

Project# New Elem #5

| Vendor | Contract Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
|--|--|-------------------|--------------------|---------------------|----------------------|
| Fund (70) Measure T Bond Funds | | | | | Dalatice |
| Department of Toxic Substance Control | DTSC FEES | CL110135 | | | |
| Department of Toxic Substance Control | DTSC Fees | CL99439 | \$432.41 | \$432.41 | \$0.00 |
| douglas e barnhart | Construction Management | C12114 | \$2,767.72 | \$2,767.72 | \$0.00 |
| Flores Lund Consultants | Civil Engineer | C11749 | \$50,000.00 | \$0.00 | \$50,000.00 |
| Flores Lund Consultants | Topographic & Boundary Surveys | C11749 | \$446.25 | \$446.25 | \$0.00 |
| Inland Foundation Eng Inc | Geotechnical Investigation, Geological/Seismic | P53708 | \$16,418.50 | \$16,418.50 | \$0.00 |
| | & Flood Review | P33708 | \$8,568.00 | \$8,568.00 | \$0.00 |
| Marshall L. McIntyre | Appraisal | CL123653 | \$1,600.00 | \$1,600.00 | \$0.00 |
| PJHM | Architect Fees | C11824 | \$661,900.00 | \$344,760.00 | \$317,140.00 |
| Planning Center | CEQA Doc's | P52768 | \$22,208.47 | \$22,208.47 | \$0.00 |
| Planning Center | Environmental Assessment | P52882 | \$6,771.34 | \$6,771.34 | \$0.00 |
| Planning Center | Health Risk Assessment | P56413 | \$2,728.00 | \$2,728.00 | \$0.00 |
| Planning Center | Environmental Impact Report | P57837 | \$8,749.57 | \$8,749.57 | \$0.00 |
| Planning Center | Augment Environmental Impact Review | P6000745 | \$3,750.00 | \$0.00 | |
| Riverside County Airport Land Use Commission | ALUC Review | RC18383 | \$245.00 | \$245.00 | \$3,750.00 \$0.00 |
| Riverside County Clerk | Dept Fish & Game Fee | CL119873 | \$4.075.50 | | |
| homas Olsen Associates | Biological Study | P53036 | \$1,275.50 | \$1,275.50 | \$0.00 |
| | | | \$1,912.50 | \$1,912.50 | \$0.00 |
| | Totals for Fund (70) Measure T Bond Funds - | 16 detail records | \$789,773.26 | \$418,883.26 | \$370,890.00 |

Hemet Unified School District Expenditure Report Currie Ranch

Measure T Bond Allocation

| Developer Fees State Funds | \$ 12,000,000.00 205,436.00 to be determined |
|----------------------------|--|
| Total Project Budget | 12,205,436.00 |
| | |
| Current Measure T Budget * | \$ 1,000,000.00 |
| Committed to Date | 848,087.95 |
| Bond Balance | \$ 151,912.05 |

^{*} Additional \$1,000,000 to be allocated from 07/08 bond sale.

^{*} Additional \$10,000,000 to be allocated from 12/13 bond sale.

Hemet Unified School District

CURRIE RANCH ELEMENTARY

Project# New Elem #12

| 11743 11936 11673(70) detail records | \$50,000.00 \$20,223.00 \$777,864.95 | \$0.00 \$4,567.75 \$536,893.33 | \$50,000.00 \$15,655.25 \$240,971.62 |
|--|--|--------------------------------------|--|
| 11936 | \$20,223.00 | | |
| | 2000019 # 01/2009 PM | | \$50,000.0 |
| 11743 | \$50,000,00 | 60.00 | |
| | | | |
| | | | |
| PO#/ Contract | Contract Amount | Payments to Date | Balance |
| | | Contract | Contract |

Hemet Unified School District Expenditure Report Issuance Costs

| Balance | \$ | 412,420.90 |
|---------------------|----------|------------|
| | | 338,205.05 |
| Committed to Date | D | 750,625.95 |
| Current Bond Budget | • | 750 005 05 |

Hemet Unified School District

ISSUANCE COSTS MEASURE T BOND

Project# Measure T Issuance Costs

| | Contract | | | | |
|--|--|----------------------|--------------------|---------------------|------------|
| Vendor | Description | PO#/ Contract | Contract Amount | Payments to Date | Balance |
| Fund (70) Measure T Bond | | | | | Dalance |
| Bowie, Arneson, Wiles & Giannone | Bond Counsel Issuance Series A | US Bank 1 | | | |
| Dale Scott & Co | Financial Advisor Issuance Series A | | \$78,000.00 | \$78,000.00 | \$0.00 |
| SourceMedia | | US Bank 2 | \$240,424.05 | \$240,424.05 | \$0.00 |
| Standard & Poors | Legal Advertising Issuance Series A | CL119025 | \$1,331.00 | \$1,331.00 | \$0.00 |
| The second secon | Rating Agency Fee Issuance Series A | US Bank 3 | \$17,500.00 | | 0 12 10.34 |
| J S Bank | Bank Administrative Fees Issuance Series A | US Bank 4 | | \$17,500.00 | \$0.00 |
| | THE RESERVE OF THE PARTY OF THE | | \$950.00 | \$950.00 | \$0.00 |
| | Totals for Fund (70) Measure T Bon | d - 5 detail records | \$338,205.05 | \$338,205.05 | \$0.00 |

HEMET UNIFIED SCHOOL DISTRICT INTER-OFFICE MEMORANDUM

From the desk of:

Richard M. Beck Assistant Superintendent, Business Services

DATE:

September 14, 2007

TO:

Citizens' Oversight Committee

SUBJECT: Hemet High School Phase III

We have attached excerpts from the August 21, 2007 Board presentation. The full presentation is posted on the District website at www.Hemetusd.k12.ca.us. Click on the Facilities Department link and then select the Hemet Modernization link.

The Governing Board is reviewing some information they requested at the September 18, 2007 Board meeting and Tina Koonce and Trittipo and Associates will present the latest information at your meeting on September 20, 2007.

RB/cl


Board Presentation for Hemet High School (Expansion / Modernization) August 21, 2007

emet Unific

School District







TRITIPO ARCHITECTURE & PLANNING






Hemet High School Facility Background

| Permanent Classrooms | Classrooms | Capacity @ 27 students |
|--|------------|------------------------|
| 1970 - Main building | 55 | 1485 |
| kitchen, locker rooms, staff offices all built for this capacity | | |
| Average classroom square footage = 851 | | |
| Acreage = 36 acres | | |
| 1984 Additions to Main Building | 6 | 162 |
| 4 science lab, dance, Art Classrooms | | |
| 2006 Stadium Addition | | |
| 2 classrooms | 2 | - |
| Additional Acreage Added 16 acres (Total 52 acres) | .11 | |
| Permanent Classroom Capacity | 63 | 1647 |

| Relocatable Classrooms | Classrooms | Capacity 25 @ 27 students 12 SDC @ 15 students | | |
|---|------------|---|--|--|
| 1984 - Over 23 years old All Priority 1 | 6 | 162 | | |
| 1985 - Over 22 years old All Priority 1 | 10 | 150 | | |
| 1987 - Over 21 years old All Priority 1 | 2 | 30 | | |
| 1989 | 1 | 27 | | |
| 1990 | 9 | 243 | | |
| 2001 | 5 | 135 | | |
| 2002 | 4 | 108 | | |
| Relocatable Classroom Capacity | 37 | 855 | | |
| TOTAL SITE CLASSROOMS | 100 | 2502 | | |





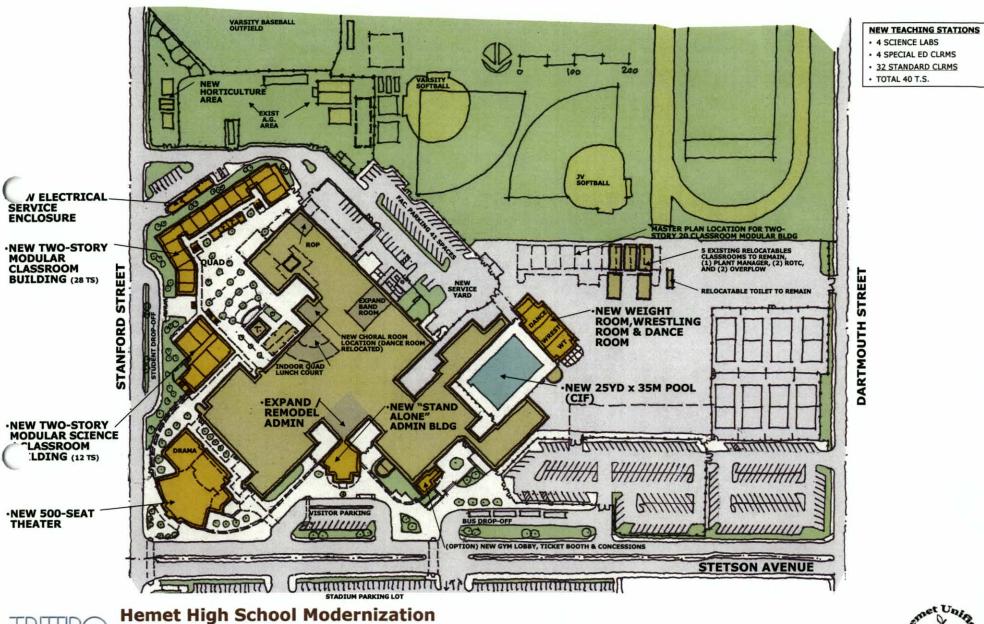

Conceptual Master Plan

School District

HEMET HIGH SCHOOL ADDITIONS AND MODERNIZATIONS CONCEPTUAL ESTIMATE 8-6-07 Summary (incl 15% contractor mark-up)

| Theater (500 Seat) | | | | \$8,804,900.25 |
|---|--------|-------|---------|-----------------|
| Science Building (4 science rooms and 8 reg classrooms) | | | | \$6,261,733.79 |
| 2-Story Regular Classrooms (24 reg classrooms + 4 special ed) | | | | \$10,574,466.20 |
| Parking and Drop-off area | | | | \$1,233,996.00 |
| New Pool | | | | \$1,845,405.00 |
| Courtyard Improvements | | | | \$114,461.80 |
| Demolition (site) | | | | \$570,714.87 |
| Landscaping (site) | | | | \$172,500.00 |
| Misc Costs Items | | | | |
| Storm Drainage Improvements | | | | \$255,875.00 |
| 2. Electrical Upgrades to accommodate new work | | | | \$603,750.00 |
| Bridge to connect 2-story buildings | | | | \$157,550.00 |
| Colonnade from new theater to gym lobby | | | | \$201,250.00 |
| 5. Site Lighting | | | | \$138,000.00 |
| Additional Buildings / Building Additions | | | | |
| Dance / Weight Room / Wrestling / Pool Equipment | | | | \$2,515,101.75 |
| 2. Administration Addition | | | | \$1,496,017.75 |
| New Electrical Utility Enclosure & Equipment | | | | \$437,074.91 |
| Modernizations | | | | |
| Administration Building | | | | \$2,055,625.00 |
| 2. ROP | | | | \$543,375.00 |
| Band Room and Choral | | | | \$855,312.50 |
| Sprinkler Upgrade to Main Complex | | | | \$898,541.00 |
| Convert Existing Theater to Interior Lunch Quad | | | | \$200,000.00 |
| | | | | |
| Subtotal | | | | \$39,935,650.82 |
| | | | | 2012/02/02 |
| Soft Costs at 20% | | | - | \$7,987,130.16 |
| | | | | |
| Total Including Soft Costs | | | | \$47,922,780.98 |
| | | | | |
| OPTIONS | | | | |
| Upgrade Lights / Data / Technology at Existing Classrooms | ŝ | | | \$925,000.00 |
| Gym / Lobby Tickets / Concessions | | | | \$592,231.60 |
| Replace bleachers in Gym & upgrade access | -12-22 | | | \$575,000.00 |
| Upgrade to Permanent Construction on 2-Story | SF | 32330 | \$55.00 | \$1,778,150.00 |
| Upgrade to Permanent Construction on Science | SF | 16485 | \$55.00 | \$906,675.00 |
| Upgrade to 800 Seat Theater + 20% soft Costs | | | | \$4,547,093.10 |
| 7. Tennis Court Lighting | | | | \$207,000.00 |
| | | | | |



