

FINAL HEMET HIGH SCHOOL PHASE 2 - FINAL BIDS & Schedule


BP#	Description		Bid Sequence
1	Demolition (Specialized Environmental)	79,000	1
	Saved \$12,520 in change orders final cost	66,480	
2	Grading & Shoring (SoCal Grading)	393,000	2
3	Site Utilities & Plumbing (JPI)		3
3	Site Utilities On Site	198,540	Bid Packages 3 & 4
3	Plumbing	904,460	1st Advertisement 7/20
3	Total Package Estimate	1,103,000	2nd Advertisement 7/27
4	Structural Steel & Metal Deck(Vulcan)		1st Jobwalk 7/27
4	Structural Steel	976,850	2nd Jobwalk 8/3
4	Misc & Ornamental	253,130	Bid Day 8/18
4	Metal Decking	268,020	Agenda Item Due 8/27
4	Total Package Estimate	1,498,000	Board Approval 9/7
			NTP 9/8
			Const. Start 9/27
5	Finish Grading/Concrete/Reinforcing/ Masonry/Fencing (Bogh)		Bid Sequence 4
5	Finish Grading	65,000	Bid Package 5 & 9
5	A/C Paving	16,800	Postponed Add#10
5	Site Concrete	585,000	Last Addendum Due 10/5
5	Bldg Concrete & Reinforcing	1,307,400	Bid Day 10/14
5	Masonry	75,300	Agenda Item Due 10/21
5	Chainlink Fencing	20,500	Board Meeting 11/2
5	Waterproofing	28,000	
5	Total Package Estimate	2,098,000	
6	Electrical (RIS Electrical)		Bid Sequence 5
6	Site Electrical	142,730	Bid Packages 6 THRU 8
6	Building Electrical	1,896,270	1st Advertisement 8/17
6	Total Package Estimate	2,039,000	2nd Advertisement 8/24
7	HVAC (Desert Air)		1st Jobwalk 8/24
7	HVAC	1,259,000	2nd Jobwalk 8/31
7	Total Package Estimate	1,259,000	Bid Day 9/21
8	FIRE SPRINKLER (JPI)		Agenda Item Due 9/24
8	Fire Sprinkler	139,000	Board Approval 10/5
8	Total Package Estimate	139,000	NTP 10/6
			Const. Start 11/8
9	Framing/Insulation/Lath & Plaster/Fireproofing/Acoustics/ Doors, Frames & Hardware	RC Luker	Bid Sequence 5
9	Metal Framing & Drywall	675,091	Bid Packages 10 thru 14
9	Insulation	137,069	1st Advertisement 9/28
9	Lath & Plaster	1,141,409	2nd Advertisement 10/5
9	Fireproofing	212,449	1st Jobwalk 10/5
9	Doors, Frames & Hardware	292,295	2nd Jobwalk 10/12
9	Acoustic Ceiling & Tackpanels	199,659	Bid Day 11/2
9	Paint & Wall Covering	274,368	Agenda Item Due 11/5
9	Aluminum Glass & Glazing	177,160	Board Approval 11/16
9	Total Package Estimate	3,109,500	NTP 11/17
10	Specialties Inland Building		Const. Start
10	Divisions 11 & 12	100,000	
10	Elevators	80,000	
10	Shade Structures	278,745	
10	Total Package Estimate	458,745	
11	Roofing/Sheet Metal/Roof Accessories	Rodgers	
11	Roofing	551,636	
11	Sheet Metal	90,361	
11	Roofing Accessories	35,545	
11	Total Package Estimate	677,542	
12	Finish Carpentry & Lab Casework	Lozano	
12	General Casework	125,000	
12	Teaching Walls	221,000	
12	Laboratory Casework & Equip	154,000	
12	Total Package Estimate	500,000	
13	Flooring (All)	Del Mar	
13	Carpet & Hard Surfaces	100,000	
13	Deck Coating	46,000	
13	Total Package Estimate	146,000	
14	Landscaping	Nature Tech	
14	Landscaping & Irrigation	94,000	
14	Total Package Estimate	94,000	
TOTAL ALL BID PACKAGES		13,581,267	
Construction Contingency @ 10%		1,358,127	
Total Budgeted Construction Costs		14,939,394	
As of 11/30/2010			
C1220811 - Closed		\$66,480	
C1220841 - Encumbered		\$6,431,000	
Unencumbered (waiting for contract signatures)		\$7,083,787	

Hemet High Phase 2: Site Utilities



Primary Sanitary Sewer In-Progress



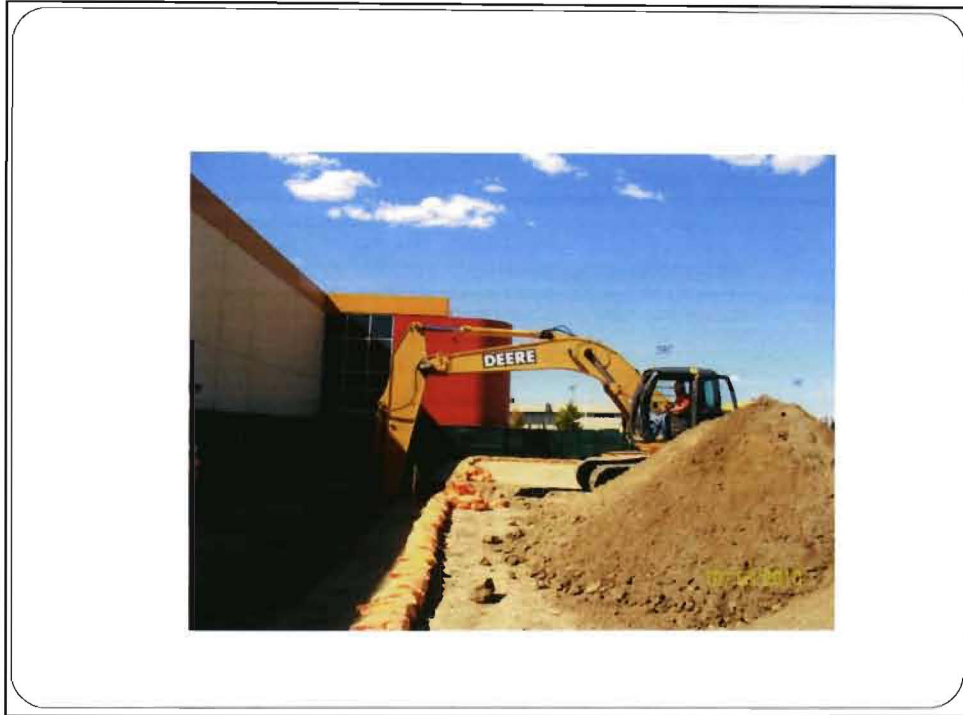

SWPPP Measures In Place



Hemet High Phase 2 – The sanitary sewer at future Theatre Building “A” is nearing completion



Backfilling sanitary sewer at building “A”



Rain Events occurred on 10/19 & 10/20



Hemet High Phase 2

Storm Drain Install at Building "B"



**Storm Drain Future Theatre
Building "A"**



Building "A" Storm Drain



S.D. In Progress at Wood Shop & Ag Area



Hemet High Phase 2

Building "C"-Under Slab Plumbing



Building "C"-Plumbing



Installation of Edison Conduits
on Stanford St.



Trenching of Edison Pathway on
Stetson Ave.

